Narayan Timbers
42/89-4, Jnanajyothinagar, 80 Feet Ring Road, Bengaluru-560 056
Phone: 99999 99999 · GSTIN: 29ABCDE1234F1Z5

WORK ORDER / JOB CARD


JOB CARD NO. **002**
DATE **19 / 09 / 2026**

CLIENT NAME	CONTACT NO.	ALT. PHONE	CARPENTER
Srinivasa B.N.	99012 75454		Hanumantha

SITE ADDRESS	CLIENT ADDRESS
No. 76, 4th Block, Sri Sai Layout, Mallathahalli, Bangalore - 560056	


FRAME ELEVATIONS

#MD1 × 1

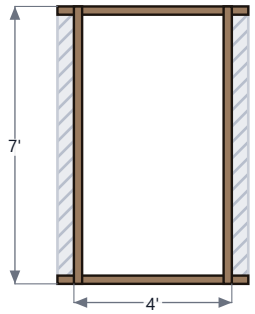


Main Door 1 · 5x3 Teak

#RD1 × 3




Room Door 1 · 5x3 Honne

#TD1 × 2




Toilet Door 1 · 4x3 Honne

#UD1 × 1




Utility Door 1 · 4x3 Sal

#WF1 × 1




Window Frames 1 · 5x3 Honne

#WF2 × 3




Window Frames 2 · 5x3 Honne

#WF3 × 2



Window Frames 3 · 5x3 Sal

#WF4 × 4



Window Frames 4 · 4x3 Sal

SCHEDULE OF OPENINGS

TAG	SIZE	NO.	SQ.FT.	PARTICULARS
#MD1	4' × 7'	1	28.00	Main Door 1 · 5x3 Teak
#RD1	3' × 7'	3	63.00	Room Door 1 · 5x3 Honne
#TD1	2' 6" × 7'	2	35.00	Toilet Door 1 · 4x3 Honne
#UD1	2' 6" × 7'	1	17.50	Utility Door 1 · 4x3 Sal
#WF1	5' 6" × 4' 6"	1	24.75	Window Frames 1 · 5x3 Honne
#WF2	3' 6" × 4' 6"	3	47.25	Window Frames 2 · 5x3 Honne
#WF3	3' × 3'	2	18.00	Window Frames 3 · 5x3 Sal
#WF4	2' × 2'	4	16.00	Window Frames 4 · 4x3 Sal
TOTAL		**17**	**249.50**	

NOTE	Door frames to site first; windows follow after slab curing.
REBATE & DESIGN	Windows and door frames 3/8" rebate; main door 1/2" with moulding.
RODS / GRILL	12 mm hexagon rod — 4'6" windows 14 rods, 3'6" windows 10 rods, 2' windows 5 rods.
REMARKS	Window frames 148.50 sq.ft · Door frames 248.50 sq.ft.

PREPARED BY | CARPENTER | CUSTOMER
